
Every replacement zone finished by 2037 at $27.1 million a year

Board of Directors, 19 January 2027, item 6: capital improvement plan 2027 to 2037. From Andrew Wells, LSLR Programme Manager, with Bethany Davidson, District Engineer. Prepared 11 January 2027.

At the capital plan's $27.1 million a year from 2027, plan revision 2 finishes all twelve zones inside the Lead and Copper Rule Improvements deadline. The last zone, RZ-06 Wexley, is finished in programme year 2037, before 1 November 2037: the running plan cost reaches $284.7 million, 10.50 years of the appropriation. The board can adopt the construction line as drafted.

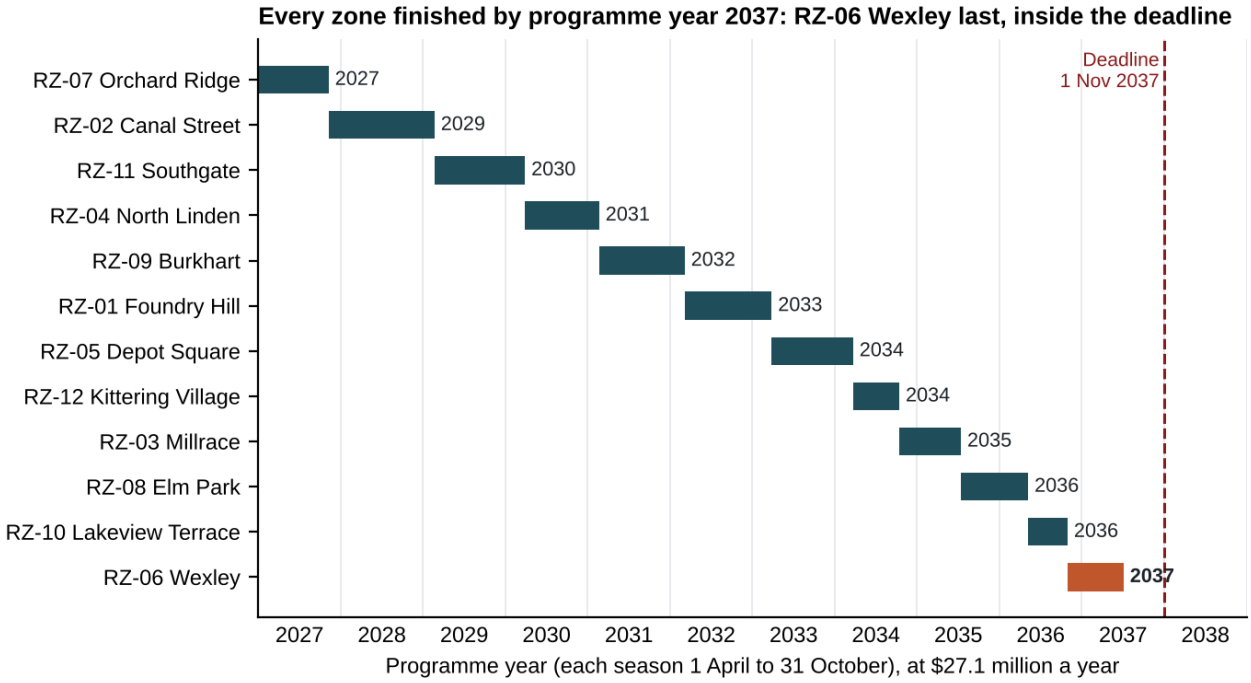

Zones in priority order; each bar runs from the zone's start to its finish on the running total of plan cost against the appropriation (plan 5.2 and 5.3).

Zone schedule

Priority	Zone	Lead and GRR lines to replace	Plan cost ($ million)	Finish year
1	RZ-07 Orchard Ridge	1,670	23.1	2027
2	RZ-02 Canal Street	2,140	34.8	2029
3	RZ-11 Southgate	1,960	29.8	2030
4	RZ-04 North Linden	1,480	24.4	2031
5	RZ-09 Burkhart	1,830	28.1	2032
6	RZ-01 Foundry Hill	1,970	28.6	2033
7	RZ-05 Depot Square	1,750	26.8	2034
8	RZ-12 Kittering Village	930	15.2	2034
9	RZ-03 Millrace	1,290	20.3	2035
10	RZ-08 Elm Park	1,380	22.1	2036
11	RZ-10 Lakeview Terrace	770	13.0	2036
12	RZ-06 Wexley	1,080	18.4	2037

Lines to the nearest ten and costs to the nearest $100,000, 2027 dollars at the 2027 unit cost schedule with one $185,000 mobilisation per zone.

How the unknown lines are costed

Plan 4.3 carries each Lead Status Unknown line at the share of lead or GRR expected among the district's lines of its construction era that have no usable tap card. Three in four of the lines with no tap card that the district has verified since 2021 were visits to one line because something pointed at it: a customer's report, a lead sampling site, a leak on the service or the 2024 consultant ranking. Those visits find lead or GRR far more often than the plan's digs will, because the plan digs every unknown line in a zone. The only lines verified without regard to what they were likely to be are on the 78 main segments where a water main replacement exposed every service, and there the shares are 0.556 before 1930, 0.316 for 1930 to 1949 and 0.083 for 1950 to 1988. At the shares across every verification on file (0.763, 0.585 and 0.217) the same plan would run to 2039.

What a full replacement cost in 2026

Paid per full replacement completed, by quarter of 2026 (Eastern time), in dollars: bid price, extra service length and restoration on each site's latest closing, with each approved change order counted once.

Contract	Contractor	Q1	Q2	Q3	Q4
2026-LSL-01	Brannigan Excavating Inc	13,890	13,494	13,416	13,673
2026-LSL-02	Tri-County Underground	14,509	13,937	13,903	13,568
2026-LSL-03	Kestrel Pipe and Utility	14,488	14,459	15,008	14,784

Tri-County Underground's vendor number changed on 13 July 2026 after its acquisition; its contract did not, and both vendor numbers are counted under 2026-LSL-02.

Access agreements in hand

Priority	Zone	Service lines with a signed access agreement
1	RZ-07 Orchard Ridge	975
2	RZ-02 Canal Street	1,217
3	RZ-11 Southgate	1,118
4	RZ-04 North Linden	954
5	RZ-09 Burkhart	1,017
6	RZ-01 Foundry Hill	857
7	RZ-05 Depot Square	889
8	RZ-12 Kittering Village	518
9	RZ-03 Millrace	626
10	RZ-08 Elm Park	663
11	RZ-10 Lakeview Terrace	368
12	RZ-06 Wexley	539

Distinct service lines with a right-of-entry agreement signed and not withdrawn at 8 January 2027, in the zone the inventory gives each line under plan revision 2; some forms signed before the revision print a different zone.
